



ATLANTIC AVENUE PROJECT UPDATE

April 17, 2023

Previous Two Weeks Summary

In the previous two weeks, the Contractor has begun installing granite curbing on Atlantic Avenue between Nantasket Avenue and Richards Road. In addition, work has continued excavating the existing pavement and widening the roadway between Stony Beach Road and Gunrock Avenue.

Two Week Look Ahead

The Contractor will continue with the installation of the new granite curb between Nantasket Avenue and Richards Road which will continue for the next one-to-two weeks. The contractor will also be grading and compacting the gravel subbase for the new and reconstructed sidewalks in this area.

Pavement reconstruction and roadway widening will continue between Stony Beach Road and Gunrock Avenue for the two weeks. The asphalt pavement will be removed, and Atlantic Avenue will have a gravel surface during this time between Stony Beach Road and approximately 300' east of Gunrock Avenue while the Contractor places new gravel and re-grades the roadway. It is anticipated the first two (of three) layers of new pavement will be paved on April 24th and 25th in this area.

Any driveways that have decorative surfaces (cobblestones, pavers, sea-shells, etc.) that are impacted by the roadway work will be temporarily stored until the Contractor is ready to re-install them.

Traffic Impacts


Expect through vehicle traffic to be detoured between School Street and Jerusalem Road during the daytime for the foreseeable future with one lane of traffic open for local traffic. Pedestrians, bicycles, school buses, and emergency vehicles will continue to be able to travel through the construction area. Access to residences, businesses and the Town Hall will also be maintained. At least one travel lane will be maintained at all times with police directing traffic as needed.

Please exercise caution traveling through Atlantic Avenue and seek alternate routes when possible. The construction may cause noise disruption during the work hours of 7:00 AM to 3:30 PM.

Questions/Concerns?

Please reach out to Joe Stigliani at jstigliani@town.hull.ma.us or the Department of Public Works at (781) 925-0900. Please keep in mind that while these updates are intended to provide as accurate and up-to-date information as possible, construction activity can change on a day-to-day basis.



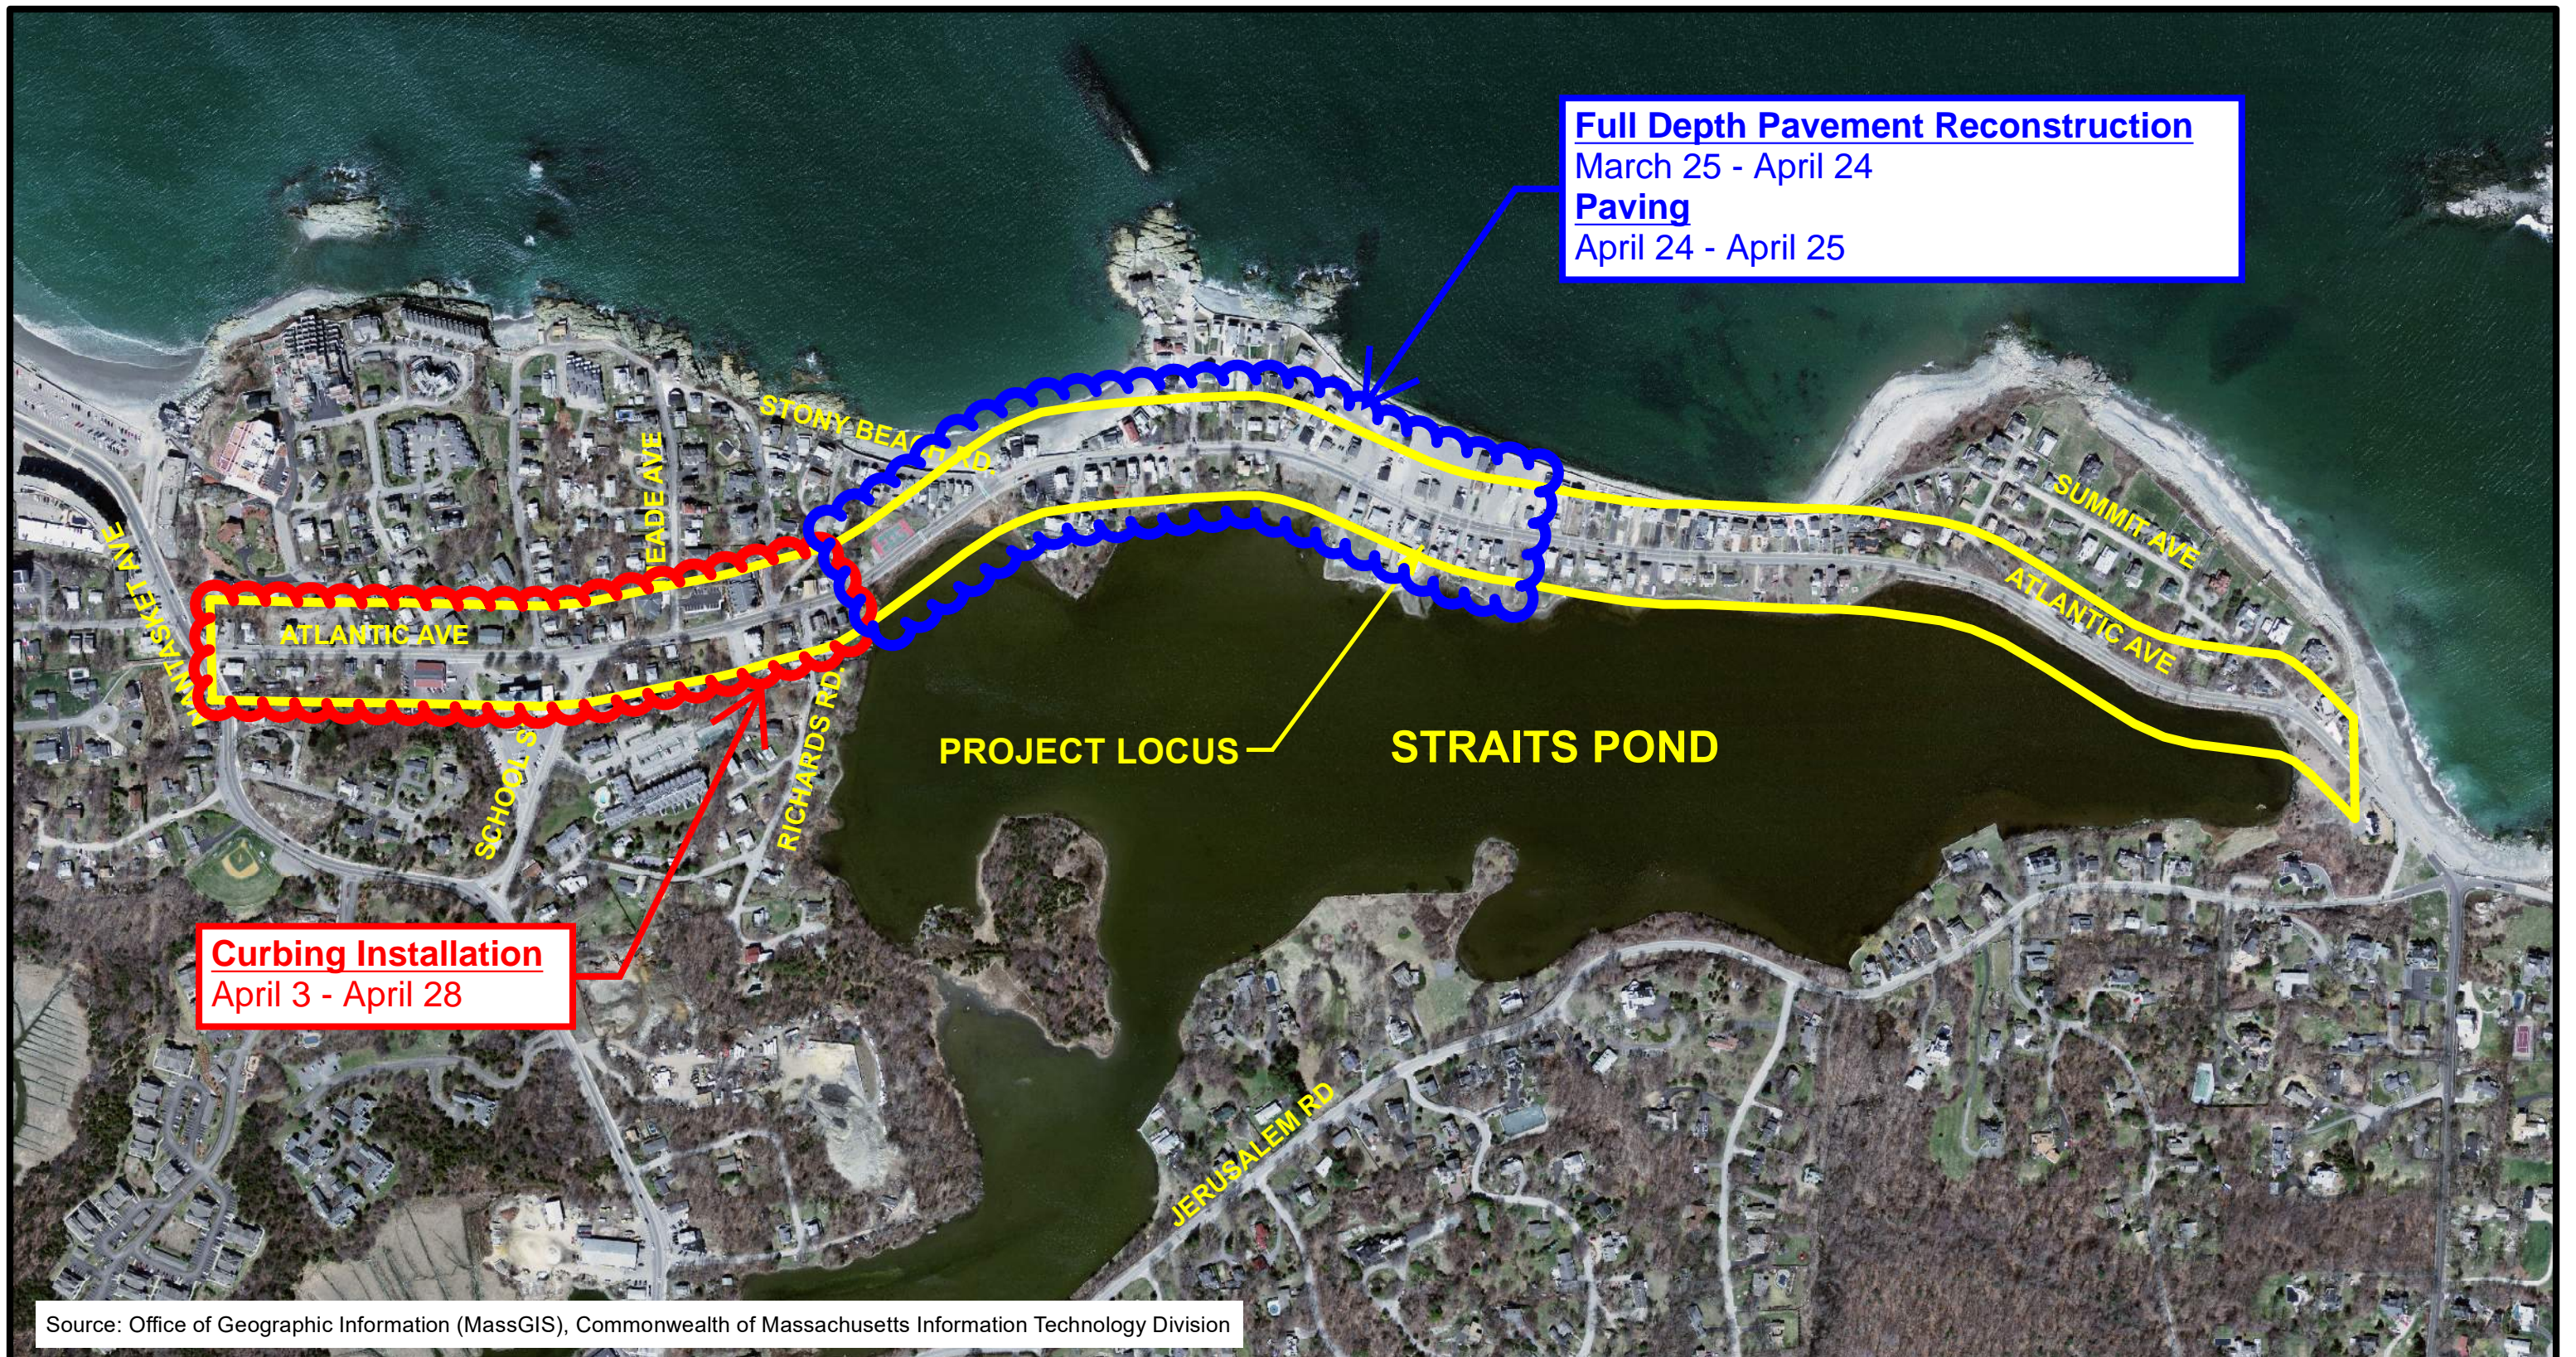

Full Depth Pavement Reconstruction
 March 25 - April 24
Paving
 April 24 - April 25

Curbing Installation
 April 3 - April 28

Source: Office of Geographic Information (MassGIS), Commonwealth of Massachusetts Information Technology Division

TOWN OF HULL, MA
ATLANTIC AVENUE RECONSTRUCTION
LOCUS MAP



PUBLIC NOTIFICATION: April 17, 2023

