



ATLANTIC AVENUE PROJECT UPDATE

April 11, 2024

Previous Two Weeks Summary

In the previous two weeks, the Contractor has been working to complete the installation of granite curbing and repair curb that was damaged over the winter, as well as raising the covers for manholes to the finished roadway grades. Construction of additional drainage structures and pipes to facilitate a raised crosswalk at the Montana Avenue intersection has also commenced.

Two Week Look Ahead

The Contractor will continue the installation of curbing and to raise manhole covers to finished grade over the next two weeks. This work will be conducted throughout the entire stretch of Atlantic Avenue. In addition, the work on the drainage system at the intersection with Montana Avenue will continue over the next week.

The other remaining work to be carried out over the next several months includes:

- Completion of sidewalk paving
- Pavement milling, mostly on side streets at the limits of work
- Paving the final surface course of pavement throughout the project.
- Installing new pavement markings and signage
- Placing loam and seeding the roadside

The Contractor is currently ahead of schedule with the project anticipated to be substantially completed by the beginning of July.

Traffic Impacts


Through vehicle traffic may be detoured as necessary between School Street and Jerusalem Road during the daytime for the foreseeable future with one lane of traffic open for local traffic. Pedestrians, bicycles, school buses, and emergency vehicles will continue to be able to travel through the construction area. Access to residences, businesses and the Town Hall will also be maintained. At least one travel lane will be maintained at all times with police directing traffic as needed.

Raised manhole covers within the roadway may pose obstacles for vehicles and bicyclists. Please exercise caution traveling through Atlantic Avenue and seek alternate routes when possible. The construction may cause noise disruption during the work hours of 7:00 AM to 3:30 PM.

Questions/Concerns?


Please visit the Town website at <https://www.town.hull.ma.us/town-manager/pages/atlantic-avenue-reconstruction-project> for information on the history of the project and the project plans.

In addition, reach out to Joe Stigliani at jstigliani@town.hull.ma.us or the Department of Public Works at (781) 925-0900. Please keep in mind that while these updates are intended to provide as accurate and up-to-date information as possible, construction activity can change on a day-to-day basis.

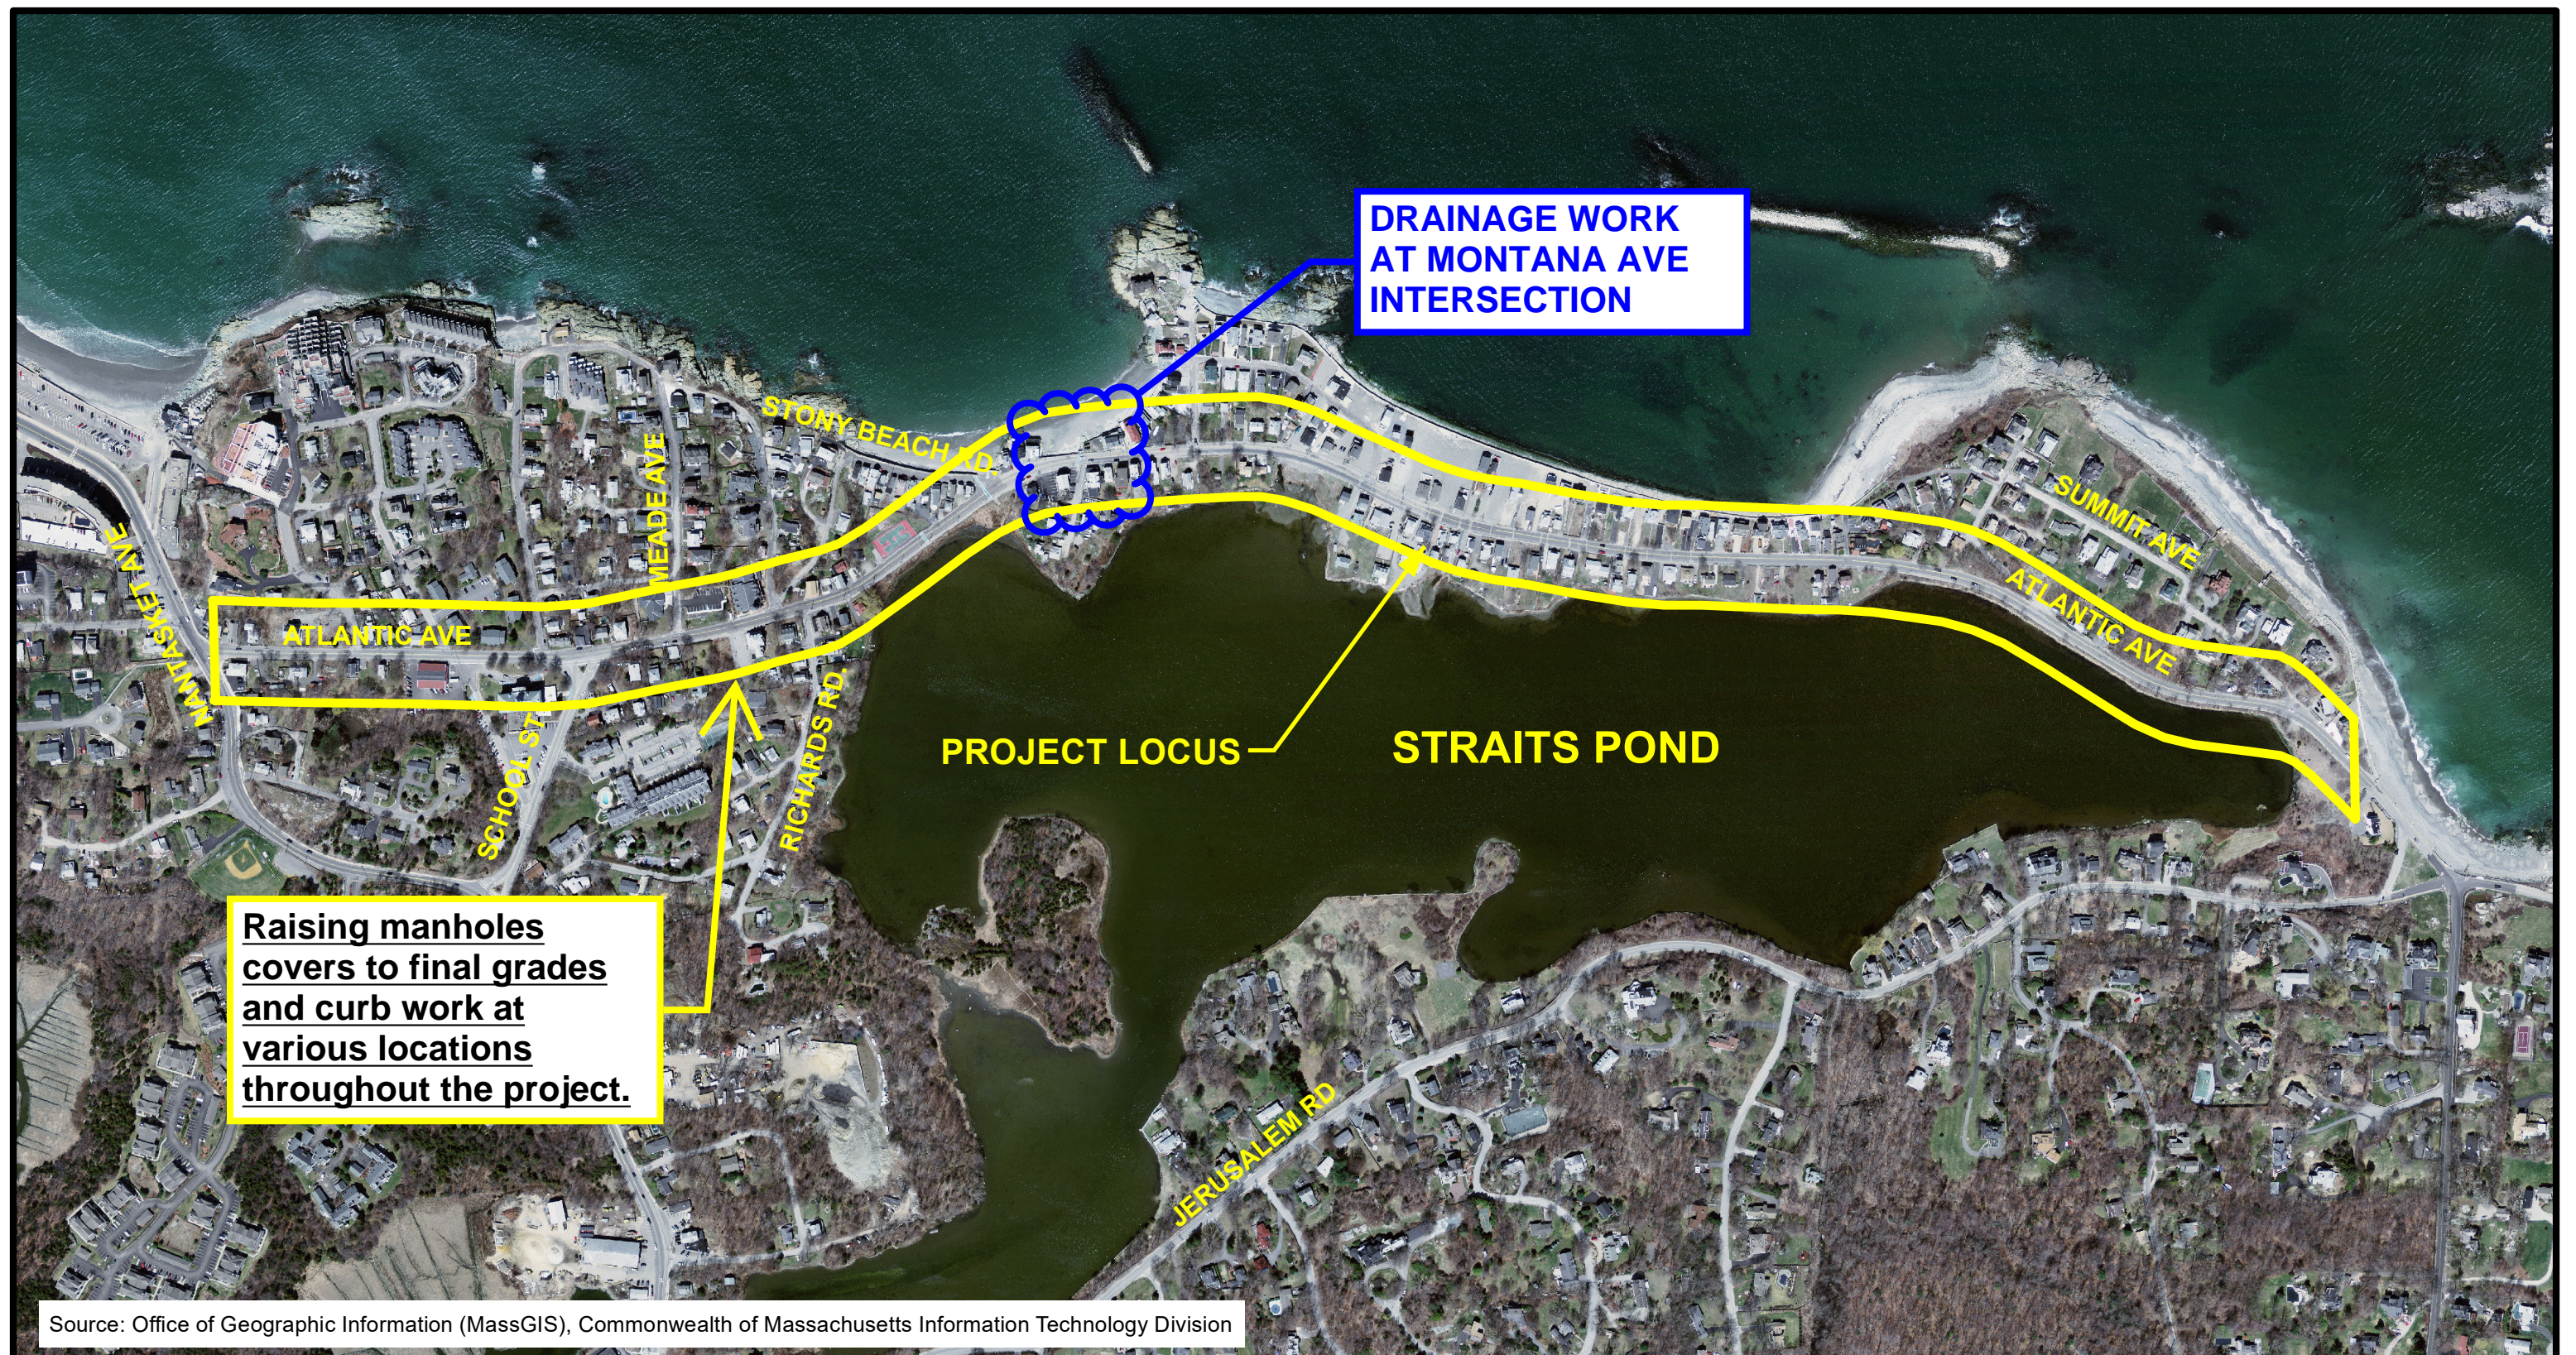

TOWN OF HULL, MA
ATLANTIC AVENUE RECONSTRUCTION

LOCUS MAP



PUBLIC NOTIFICATION: April 11, 2024

